


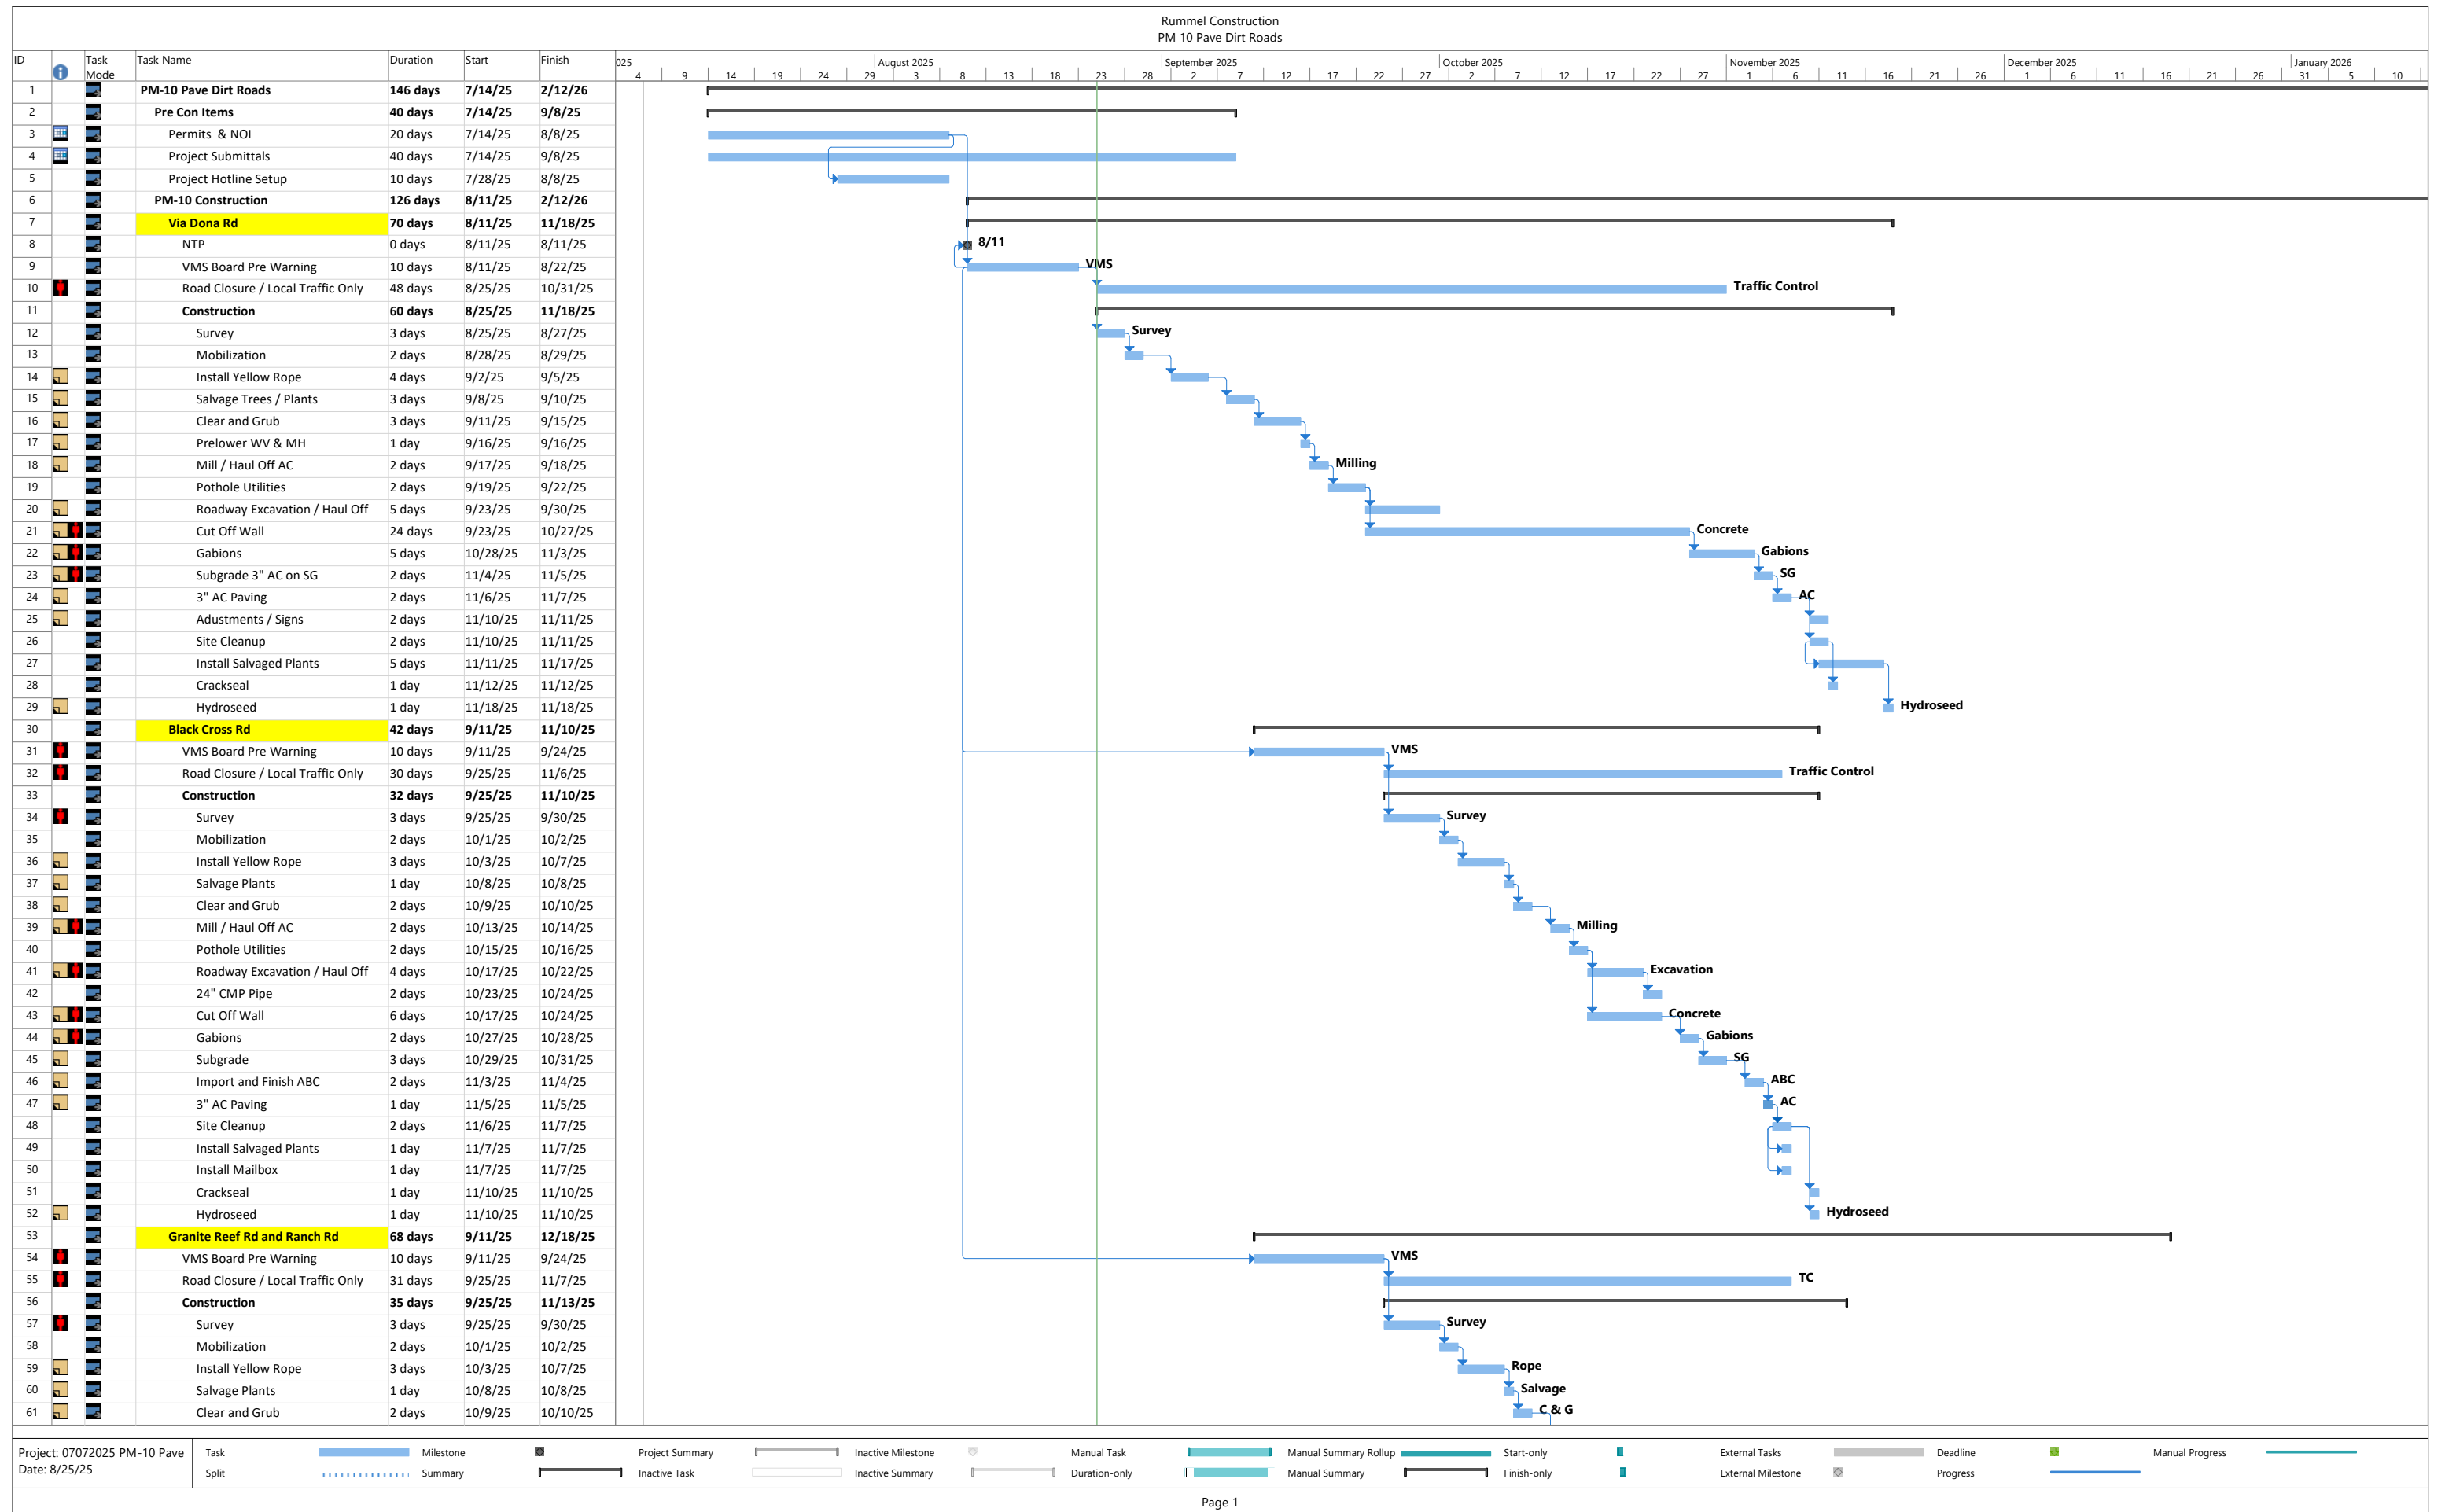

Rummel Construction
PM 10 Pave Dirt Roads

ID		Task Mode	Task Name	Duration	Start	Finish
62			Prelower WV	1 day	10/13/25	10/13/25
63			Mill / Haul Off AC	2 days	10/14/25	10/15/25
64			Pothole Utilities	3 days	10/16/25	10/20/25
65			Roadway Excavation / Haul Off	7 days	10/21/25	10/29/25
66			Rip Rap	2 days	10/30/25	10/31/25
67			Subgrade	2 days	11/3/25	11/4/25
68			Import and Finish ABC	3 days	11/5/25	11/7/25
69			3" AC Paving	1 day	11/10/25	11/10/25
70			Adjustments	1 day	11/11/25	11/11/25
71			Site Cleanup	2 days	11/11/25	11/12/25
72			Install Salvaged Plants	2 days	11/12/25	11/13/25
73			Crackseal	1 day	11/13/25	11/13/25
74			Hydroseed	1 day	11/13/25	11/13/25
75			Peak View Rd	44 days	10/16/25	12/18/25
76			VMS Board Pre Warning	10 days	10/16/25	10/29/25
77			Road Closure / Local Traffic Only	29 days	10/30/25	12/11/25
78			Construction	34 days	10/30/25	12/18/25
79			Survey	3 days	10/30/25	11/3/25
80			Mobilization	2 days	11/4/25	11/5/25
81			Install Yellow Rope	2 days	11/6/25	11/7/25
82			Salvage Plants	1 day	11/10/25	11/10/25
83			Clear and Grub	2 days	11/11/25	11/12/25
84			Prelower WV & MH	1 day	11/13/25	11/13/25
85			Mill / Haul Off AC	2 days	11/14/25	11/17/25
86			Pothole Utilities	2 days	11/18/25	11/19/25
87			Roadway Excavation / Haul Off	3 days	11/20/25	11/24/25
88			Cut Off Wall	10 days	11/20/25	12/5/25
89			Gabions	3 days	12/8/25	12/10/25
90			Subgrade 3" AC on SG	2 days	12/11/25	12/12/25
91			3" AC Paving	1 day	12/15/25	12/15/25
92			Adjustments	1 day	12/16/25	12/16/25
93			Site Cleanup	2 days	12/16/25	12/17/25
94			Install Mail Box	1 day	12/17/25	12/17/25
95			Install Salvaged Plants	1 day	12/17/25	12/17/25
96			Crackseal	1 day	12/18/25	12/18/25
97			Hydroseed	1 day	12/18/25	12/18/25
98			Smokehouse Trail	78 days	10/20/25	2/12/26
99			VMS Board Pre Warning	10 days	10/20/25	10/31/25
100			Road Closure / Local Traffic Only	28 days	11/3/25	12/12/25
101			Construction	68 days	11/3/25	2/12/26
102			Survey	3 days	11/3/25	11/5/25
103			Mobilization	2 days	11/6/25	11/7/25
104			Install Yellow Rope	2 days	11/10/25	11/11/25
105			Salvage Plants	3 days	11/12/25	11/14/25
106			Clear and Grub	2 days	11/17/25	11/18/25
107			Prelower WV & MH	1 day	11/19/25	11/19/25
108			Mill / Haul Off AC	2 days	11/20/25	11/21/25
109			Pothole Utilities	2 days	11/24/25	11/25/25
110			Roadway Excavation / Haul Off	7 days	11/26/25	12/8/25
111			Subgrade	2 days	12/9/25	12/10/25
112			Import and Finish ABC	3 days	12/11/25	12/15/25
113			3" AC Paving	1 day	12/16/25	12/16/25
114			Adjustments	1 day	12/17/25	12/17/25
115			Site Cleanup	2 days	12/17/25	12/18/25
116			Install Salvaged Plants	1 day	12/18/25	12/18/25
117			Crackseal	1 day	12/19/25	12/19/25
118			Hydroseed	1 day	12/19/25	12/19/25
119			Subtantial Completion	0 days	12/19/25	12/19/25
120			Warranty Establishment Period	90 days	11/15/25	2/12/26

The Gantt chart displays the project timeline from August 2025 to January 2026. It features three main task sections:

- Peak View Rd (Yellow Highlighted):** Includes tasks like VMS Board Pre Warning, Road Closure, Survey, Mobilization, Install Yellow Rope, Salvage Plants, Clear and Grub, Prelower WV & MH, Mill / Haul Off AC, Pothole Utilities, Roadway Excavation / Haul Off, Cut Off Wall, Gabions, Subgrade 3" AC on SG, 3" AC Paving, Adjustments, Site Cleanup, Install Mail Box, Install Salvaged Plants, Crackseal, and Hydroseed.
- Smokehouse Trail (Yellow Highlighted):** Includes tasks like VMS Board Pre Warning, Road Closure, Survey, Mobilization, Install Yellow Rope, Salvage Plants, Clear and Grub, Prelower WV & MH, Mill / Haul Off AC, Pothole Utilities, Roadway Excavation / Haul Off, Subgrade, Import and Finish ABC, 3" AC Paving, Adjustments, Site Cleanup, Install Salvaged Plants, Crackseal, Hydroseed, Subtantial Completion, and Warranty Establishment Period.
- Warranty Establishment Period (Grey Highlighted):** A long-term task spanning from November 2025 to February 2026.

The chart
